


Southern Gas Corridor to Europe




The Southern Corridor investors




Trans-Adriatic Pipeline (TAP)

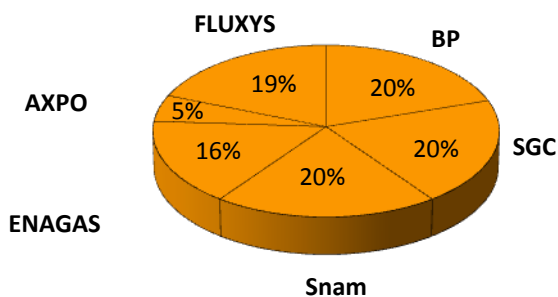

Trans-Anatolian Pipeline (TANAP)

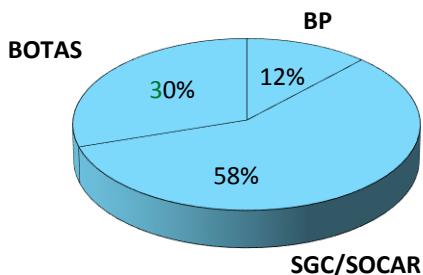

Shah Deniz 2 and SCP Expansion (SCPX)

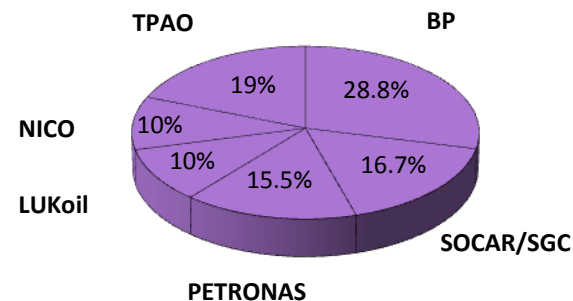



TANAP pipe-laying

- Construction of the 56" pipeline ongoing on all 3 construction sections using pipe from both Turkish and Chinese mills.
- Around 700 km welded and 800 km stringed.
- Site preparation commenced at First Gas Stations.
- Schedule under pressure – front-end activities essentially on target but back-end activities lagging behind.



- Pipeline construction started in both Greece and Albania
- Independent Transmission System Operator certification received.
- Timely approval of permits is a key area of risk that could impact project schedule.
 - Offshore programme has now officially been rescheduled to the second season (2017/18) due to delay in Olive tree removal permit in Italy.
 - Work must start in November window to avoid further delays.
